

ঢাকা পানি সরবরাহ ও পয়ঃ নিষ্কাশন কর্তৃপক্ষ

নির্বাহী প্রকৌশলীর কার্যালয়

এফ.এম বিভাগ-২, ঢাকা ওয়াসা।

দারুস সালাম রোড, মিরপুর, ঢাকা-১২১৬



অফিস টেলিফোনঃ ০২-৪৮০৩১৯৫০, ০২-৪৮০৩১৬৪৬, মোবাইল-০১৮৭৯৮২৯৭০০, E-mail:- ee_fm2@dwasa.org.bd

স্মারক নং-৪৬.১১৩.৪২৪.০০.০০.২০২৬. ৩৭২

তারিখঃ-০৬/০৯/২০২৬

নির্বাহী প্রকৌশলী,
সংগ্রহ বিভাগ-২,
ঢাকা ওয়াসা।

বিষয়ঃ ঢাকা ওয়াসার এফ.এম বিভাগ এর জন্য দি আলফা ইঞ্জিনিয়ারিং কর্তৃক সরবরাহকৃত ১০০ ঘনমিটার/ঘন্টা ১২৫মিটার হেড এর ২(দুই) সেট সাব-মার্সিবল পাম্প-মোটর গভীর নলকূপে স্থাপন ও পারফরম্যান্স রিপোর্ট প্রদান প্রসঙ্গে।

সূত্রঃ- স্মারক নং- ৪৬.১১৩.৪২৪.০০.০০.০৪৭.২০২৫-১৩১ তারিখ-৩১/০৮/২০২৬ ইং

উপর্যুক্ত বিষয় ও সূত্রের প্রেক্ষিতে জানানো যাচ্ছে যে, সংগ্রহ বিভাগ-২ এর মাধ্যমে দি আলফা ইঞ্জিনিয়ারিং কর্তৃক সরবরাহকৃত ১০০ ঘনমিটার/ঘন্টা ১২৫মিটার হেড সাব-মার্সিবল পাম্প মোটর হতে ০২(দুই) সেট পাম্প মোটর এফ.এম.বিভাগ-২ এর আওতাধীন ২টি পাম্প-স্টেশনে স্থাপন করা হয়েছে। উক্ত স্থাপনকৃত পাম্প-মোটরের পারফরম্যান্স রিপোর্ট তৈরী করতঃ এতদসংগে সংযুক্ত করা হল।

এমতাবস্থায়, কর্তৃপক্ষের কাজের স্বার্থে প্রয়োজনীয় ব্যবস্থা গ্রহণের জন্য অনুরোধ করা হ'ল।

(Signature)
০৬/০৯/২০২৬

মোঃ নওশাদা আলম

নির্বাহী প্রকৌশলী

এফ.এম. বিভাগ-২, ঢাকা ওয়াসা।

অনুলিপিঃ

- ১। প্রধান প্রকৌশলী, ঢাকা ওয়াসা।
- ২। তত্ত্বাবধায়ক প্রকৌশলী, আর.পি.ইএন্ড এম সার্কেল, ঢাকা ওয়াসা।
- ৩। নির্বাহী প্রকৌশলী, ভান্ডার বিভাগ, ঢাকা ওয়াসা।
- ৪। দি আলফা ইঞ্জিনিয়ারিং, হাউজ-২৩, রোড-০১, পূর্ব মেরুল বাজা, ঢাকা-১২১২।
- ৫। অফিস

(Signature)
৩.৮.২৬


SA/E
(Signature)
06.09.26
Md. Mazharul Islam
Executive Engineer
Procurement Division-2
Dhaka WASA


পারফরম্যান্স রিপোর্ট

বিষয় : ঢাকা ওয়াসার এফ.এম বিভাগ এর জন্য দি আলফা ইঞ্জিনিয়ারিং কর্তৃক সরবরাহকৃত ১০০ ঘনমিটার/ঘন্টা ১২৫মিটার হেড এর ২ সেট সাব-মার্সিবল পাম্প-মোটর গভীর নলকূপে স্থাপন ও পারফরম্যান্স রিপোর্ট প্রদান প্রসঙ্গে।

সূত্রঃ- স্মারক নং-৪৬.১১৩.৪২৮.০০.০০.০৪৭.২০২৫-১৩১ তাং-৩১/০৮/২০২৬ ইং

ক্রঃ নং	পাম্প মোটর ক্যাপাসিটি			সিরিয়াল নং		স্থাপনকৃত কূপের নাম	পানি উৎপাদন (লিঃ/মিঃ)	ভোল্টেজ (ভোল্ট)	কারেন্ট	ফ্রিকুয়েন্সি	ফলাফল
	ঘঃমিঃ/ঘঃ	হেড	ব্রান্ড	মোটর অংশ	পাম্প অংশ						
১	১০০	১২৫	MSP	55580875260 32299PA2	260244763	গুলশান-৭৪	১৮০০	৪০০	৮৫	৪৮	সন্তোষ জনক
২	১০০	১২৫	MSP	55580857526 032343PA2	260244622	ইব্রাহীমপুর-২	১৭০০	৪০০	৮০	৪৬	সন্তোষ জনক


মোঃ আসাদুজ্জামান
উপ- সহকারী প্রকৌশলী
এফ.এম. বিভাগ-২, ঢাকা ওয়াসা।


6.09.26
মোঃ মাহবুবুল হক প্রামানিক
সহকারী প্রকৌশলী
এফ.এম. বিভাগ-২, ঢাকা ওয়াসা।


06/09/2026
মোঃ নওশাদ আলম
নির্বাহী প্রকৌশলী
এফ.এম. বিভাগ-২, ঢাকা ওয়াসা।



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

Military Institute of Science and Technology (MIST)



TEST REPORT FOR SUBMERSIBLE PUMP

Date: 31-08-2026

CLIENT : Executive Engineer
Shongroh Bivag - 2
Dhaka Wasa, Dhaka

CLIENT'S REF : 46.113.428.00.00.048.2025-74
Date: 22-07-2026

MIST (ME) REF : 23.12.0902.006.021.008.31.08.2026/Pump94

NAME OF SUPPLIER : The Alpha Engineering

TEST CONDUCTED BY

DEPARTMENT OF MECHANICAL ENGINEERING
MILITARY INSTITUTE OF SCIENCE AND TECHNOLOGY


DHAKA-1216

SDF/AE
31.08.26

Signature
31.08.26



X7A9V1BG



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

Military Institute of Science and Technology (MIST)



SAMPLES SUPPLIED

: Submersible Pump
125.00 m (410.10 ft)
100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min)
Pump No: 260244763
Motor No: 5558087526032299PA2

Submersible Pump
125.00 m (410.10 ft)
100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min)
Pump No: 260244622
Motor No: 55580857526032343PA2



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

Military Institute of Science and Technology (MIST)





RESULT SHEET

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244763	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(a)
Motor No:	5558087526032299PA2	Pump ID:	20260825-0682
Date of Test:	25-08-2026	Ambient Temperature:	32°C
Relative Humidity:	67%	Water Temperature:	30°C
Speed (No Load):	2960 RPM	Operating Voltage:	400±2 V

No	Discharge (m ³ /hr)	Total Head (m)	Input Power (kW)	Combined Efficiency (%)
1	69.27	156.61	50.00	59.10
2	83.12	149.60	52.33	64.73
3	91.87	142.59	53.91	66.19
4	95.57	139.79	54.54	66.73
5	99.23	136.42	54.98	67.07
6	102.50	132.77	55.26	67.09
7	108.80	125.05	55.82	66.40
8	114.77	117.48	56.02	65.56
9	121.74	107.51	56.03	63.64
10	126.37	100.50	55.84	61.96
11	134.18	86.46	55.53	56.91

1. At maximum combined efficiency of 67.09%, the pump delivered 102.50 m³/hr (1.01 ft³/sec, 1,708.68 l/min) discharge, at a total head of 132.77 m (435.60 ft) with an input power of 55.26 kW.
2. At 100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min) rated discharge, the pump developed 135.56 m (444.75 ft) of total head with 67.08% combined efficiency.

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam, psc Head, ME Dept Mohammad Shariful Islam Brigadier General Head of Mechanical Engineering Dept. MIST, Mirpur Cantonment, Dhaka
--	---



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

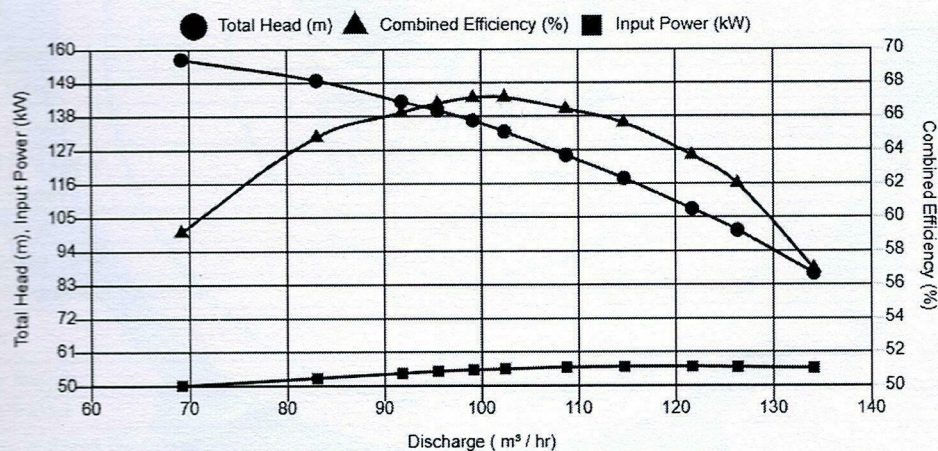
Military Institute of Science and Technology (MIST)





PERFORMANCE CURVE

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244763	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(a)
Motor No:	5558087526032299PA2	Pump ID:	20260825-0682
Date of Test:	25-08-2026	Ambient Temperature:	32°C
Relative Humidity:	67%	Water Temperature:	30°C
Speed (No Load):	2960 RPM	Operating Voltage:	400±2 V

Performance Graph



1. At maximum combined efficiency of 67.09%, the pump delivered 102.50 m³/hr (1.01 ft³/sec, 1,708.68 l/min) discharge, at a total head of 132.77 m (435.60 ft) with an input power of 55.26 kW.
2. At 100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min) rated discharge, the pump developed 135.56 m (444.75 ft) of total head with 67.08% combined efficiency.

Prepared By  Tariq Mahub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam, psc Head, ME Dept
---	--

Mohammad Shariful Islam
Brigadier General
Head of Mechanical Engineering Dept.
MIST, Mirpur Cantonment, Dhaka



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)



Military Institute of Science and Technology (MIST)



TEST OF DIFFERENT PARAMETERS

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244763	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(a)
Motor No:	5558087526032299PA2	Pump ID:	20260825-0682
Date of Test:	25-08-2026	Ambient Temperature:	32°C
Relative Humidity:	67%	Water Temperature:	30°C
Speed (No Load):	2960 RPM	Operating Voltage:	400±2 V

Pump	
Pump Bowl Diameter	200 mm
Rated Head	125.00 m
Rated Discharge	100.00 m ³ /hr
Speed (No Load)	2960 rpm
No of Stages	07
Installation	Vertical Installation
Non-return Valve	Built in with the pump
Cable Guards and Channels	2X Cable guard fitted outside the pump bowl
Motor	
Power Supply	AC, 3-Phase, 400±2 V, 50Hz
Power Factor	0.82
Current at Rated Discharge	99.53 amp
Rated Power	55.35 kW
Starting Method	Star Delta Starter
Motor Diameter	190 mm
Cable Size (with insulation)	3x56.74 mm ²
Cable Size (without insulation)	3x31.37 mm ²
Cable Length	3.4 m

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam Head, ME Dept Mohammad Shariful Islam Brigadier General Head of Mechanical Engineering Dept. MIST, Mirpur Cantonment, Dhaka
---	--



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

Military Institute of Science and Technology (MIST)





RESULT SHEET

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244622	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(b)
Motor No:	55580857526032343PA2	Pump ID:	20260827-0683
Date of Test:	27-08-2026	Ambient Temperature:	34°C
Relative Humidity:	54%	Water Temperature:	32°C
Speed (No Load):	2950 RPM	Operating Voltage:	400±2 V

No	Discharge (m ³ /hr)	Total Head (m)	Input Power (kW)	Combined Efficiency (%)
1	76.20	153.10	50.69	62.70
2	81.76	149.60	51.85	64.26
3	91.55	142.59	53.96	65.90
4	95.46	139.43	54.51	66.52
5	99.00	136.63	54.99	67.01
6	101.89	132.91	55.01	67.06
7	104.73	129.61	55.37	66.78
8	110.68	121.54	55.99	65.45
9	121.28	107.51	56.27	63.12
10	126.23	100.50	56.03	61.68
11	134.50	86.46	55.42	57.16

1. At maximum combined efficiency of 67.06%, the pump delivered 101.89 m³/hr (1.00 ft³/sec, 1,698.51 l/min) discharge, at a total head of 132.91 m (436.05 ft) with an input power of 55.01 kW.
2. At 100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min) rated discharge, the pump developed 135.34 m (444.03 ft) of total head with 67.03% combined efficiency.

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam, psc Head, ME Dept
--	--

Mohammad Shariful Islam
Brigadier General
Head of Mechanical Engineering Dept.
MIST, Mirpur Cantonment, Dhaka



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)

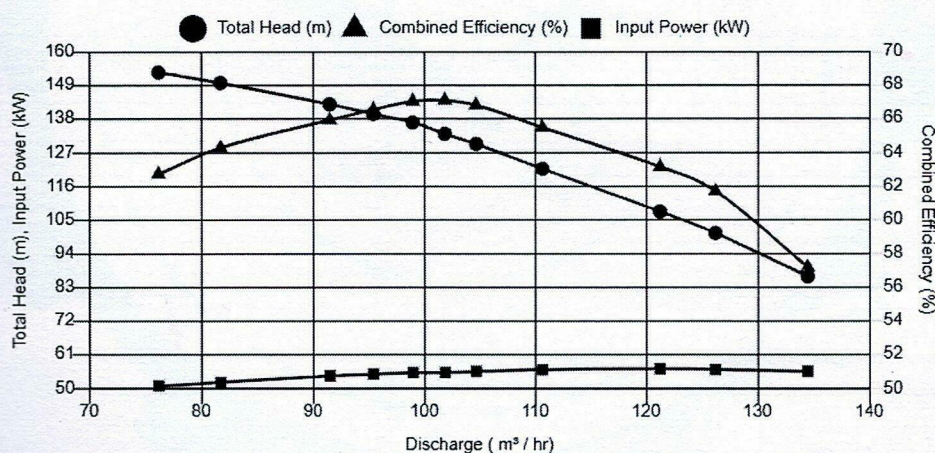
Military Institute of Science and Technology (MIST)





PERFORMANCE CURVE

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244622	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(b)
Motor No:	55580857526032343PA2	Pump ID:	20260827-0683
Date of Test:	27-08-2026	Ambient Temperature:	34°C
Relative Humidity:	54%	Water Temperature:	32°C
Speed (No Load):	2950 RPM	Operating Voltage:	400±2 V

Performance Graph



1. At maximum combined efficiency of 67.06%, the pump delivered 101.89 m³/hr (1.00 ft³/sec, 1,698.51 l/min) discharge, at a total head of 132.91 m (436.05 ft) with an input power of 55.01 kW.
2. At 100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min) rated discharge, the pump developed 135.34 m (444.03 ft) of total head with 67.03% combined efficiency.

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam, psc Head, ME Dept Mohammad Shariful Islam Brigadier General Head of Mechanical Engineering Dept. MIST, Mirpur Cantonment, Dhaka
---	---



Center for Advisory and Testing Services [CATS]

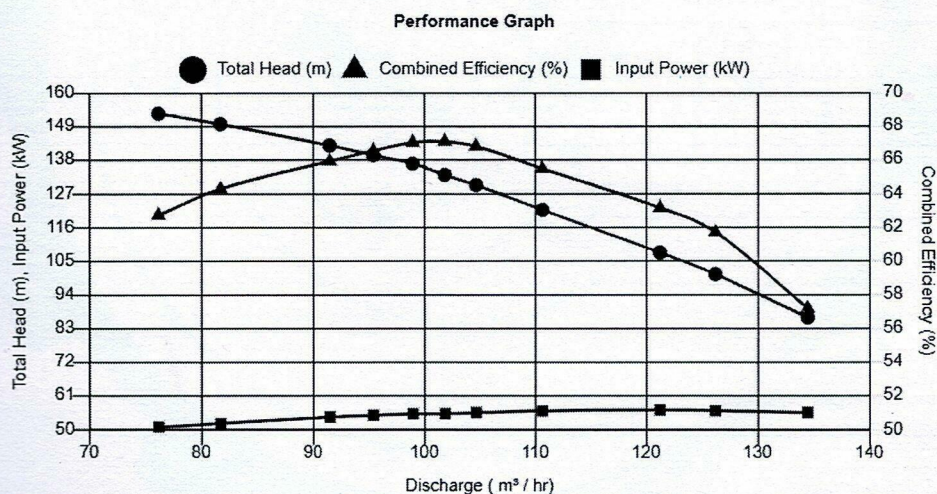
Department of Mechanical Engineering (ME)

Military Institute of Science and Technology (MIST)





PERFORMANCE CURVE

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244622	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(b)
Motor No:	55580857526032343PA2	Pump ID:	20260827-0683
Date of Test:	27-08-2026	Ambient Temperature:	34°C
Relative Humidity:	54%	Water Temperature:	32°C
Speed (No Load):	2950 RPM	Operating Voltage:	400±2 V



1. At maximum combined efficiency of 67.06%, the pump delivered 101.89 m³/hr (1.00 ft³/sec, 1,698.51 l/min) discharge, at a total head of 132.91 m (436.05 ft) with an input power of 55.01 kW.
2. At 100.00 m³/hr (0.98 ft³/sec, 1,667.00 l/min) rated discharge, the pump developed 135.34 m (444.03 ft) of total head with 67.03% combined efficiency.

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam, psc Head, ME Dept Mohammad Shariful Islam Brigadier General Head of Mechanical Engineering Dept. MIST, Mirpur Cantonment, Dhaka
--	---



Center for Advisory and Testing Services [CATS]

Department of Mechanical Engineering (ME)



Military Institute of Science and Technology (MIST)



TEST OF DIFFERENT PARAMETERS

Pump Type:	Submersible Pump	Client:	Executive Engineer Shongroh Bivag - 2 Dhaka Wasa, Dhaka
Head:	125.00 m (410.10 ft)	Client's Ref and Date:	46.113.428.00.00.048.2025-74 Date: 22-07-2026
Discharge:	100.00 m ³ /hr (0.98 ft ³ /sec, 1,667.00 l/min)	Name of Supplier:	The Alpha Engineering
Pump No:	260244622	MIST (ME) Ref:	23.12.0902.006.021.008.31.08.2026/Pump94(b)
Motor No:	55580857526032343PA2	Pump ID:	20260827-0683
Date of Test:	27-08-2026	Ambient Temperature:	34°C
Relative Humidity:	54%	Water Temperature:	32°C
Speed (No Load):	2950 RPM	Operating Voltage:	400±2 V

Pump	
Pump Bowl Diameter	200 mm
Rated Head	125.00 m
Rated Discharge	100.00 m ³ /hr
Speed (No Load)	2950 rpm
No of Stages	07
Installation	Vertical Installation
Non-return Valve	Built in with the pump
Cable Guards and Channels	2X Cable guard fitted outside the pump bowl
Motor	
Power Supply	AC, 3-Phase, 400±2 V, 50Hz
Power Factor	0.81
Current at Rated Discharge	98.02 amp
Rated Power	55.11 kW
Starting Method	Star Delta Starter
Motor Diameter	190 mm
Cable Size (with insulation)	3x56.74 mm ²
Cable Size (without insulation)	3x31.37 mm ²
Cable Length	2X3.4 m

Prepared By  Tariq Mahbub Assistant Professor, ME Dept	Approved By  Brig Gen Mohammad Shariful Islam Head, ME Dept Brigadier General Head of Mechanical Engineering Dept. MIST, Mirpur Cantonment, Dhaka
--	--

ঢাকা পানি সরবরাহ ও পয়ঃ নিষ্কাশন কর্তৃপক্ষ

ওয়াসা

নির্বাহী প্রকৌশলীর কার্যালয়
সংগ্রহ বিভাগ-২, ওয়াসা ভবন (৬ষ্ঠ তলা),
৯৮, কাজী নজরুল ইসলাম এভিনিউ, কাওরান বাজার, ঢাকা-১২১৫।
WebSite: www.dwasa.org.bd Phone: 41010230

কারিগরি পরীক্ষণ ও গ্রহন কমিটি রিপোর্ট

চুক্তি নং-	%	৪৬.১১৩.৪২৮.০০.০০.০৪৭.২৫/cGP/সিএ-১৪;	তারিখঃ ২৯/১২/২০২৫ ইং।
সরবরাহ আদেশ স্মারক নং-	%	৪৬.১১৩.৪২৮.০০.০০.০৪৭.২০২৫-৬০৮;	তারিখঃ ০৮/০১/২০২৬ইং।
কাজের নাম	%	Procurement of 100 Cubic meter per hour 125 meter head capacity submersible Pump-Motor sets for F.M Division, DWASA।	
সরবরাহকারীর নাম	%	দি আলফা ইঞ্জিনিয়ারিং, হাউজ-২৩, রোড-০১, পূর্ব মেরুল, বাড়ড়া, ঢাকা-১২১২।	
সরবরাহকারী বিভাগের নাম	%	সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা।	
ব্যবহারকারী বিভাগের নাম	%	ঢাকা ওয়াসার এফ. এম. বিভাগ।	
সরবরাহের স্থান	%	ভান্ডার বিভাগ, ঢাকা ওয়াসা।	
সরবরাহের তারিখ	%	২১/০৭/২০২৬ ইং।	যৌথ পরিদর্শনের তারিখঃ ২২/০৭/২০২৬ ইং।

ক্র. নং.	মালামালের বিবরণ	চুক্তি অনুযায়ী মালামালের পরিমাণ	একই কিস্তিতে দেয় মালামালের পরিমাণ
১।	100 m ³ /hr.125 meter head submersible Pump- Motor.	১৮ (আঠারো) সেট	১৮ (আঠারো) সেট

Sl. No.	Pump serial	Sl. No.	Pump serial	Sl. No.	Pump serial	Country of Origin
1	260244777	7	260244766	13	260244765	Turkey
2	260244767	8	260244763	14	260244768	
3	260244775	9	260244622	15	260244771	
4	260244772	10	260244761	16	260244762	
5	260244774	11	260244764	17	260244776	
6	260244769	12	260244773	18	260244770	

Sl. No.	Motor serial	Sl. No.	Motor serial	Sl. No.	Motor serial	Country of Origin
1	555808 752603 2308 PA2	7	555808 752603 2317 PA2	13	555808 752603 2312 PA2	Turkey
2	555808 752603 2338 PA2	8	555808 752603 2363 PA2	14	555808 752601 0570 PA2	
3	580855 752603 2345 PA2	9	555808 752603 2311 PA2	15	555808 752603 2324 PA2	
4	555808 752603 2342 PA2	10	555808 752603 2360 PA2	16	555808 752603 2364 PA2	
5	555808 752603 2298 PA2	11	555808 752603 2337 PA2	17	555808 752603 2299 PA2	
6	555808 752603 2304 PA2	12	580855 752603 2300 PA2	18	555808 752603 2343 PA2	

যৌথ পরিদর্শন কমিটি কর্তৃক সমুদয় মালামাল পরিদর্শন করা হইল এবং তা বাহ্যিকভাবে সঠিক পাওয়া গেল। বাহ্যিকভাবে সঠিক পাওয়ায় টেষ্টের জন্য নমুনা সংগ্রহ করা হল।
এম.আই.এস.টি. হইতে প্রাপ্ত টেষ্ট রিপোর্টের ভিত্তিতে সমুদয় মালামাল চূড়ান্তভাবে গ্রহণ/বাতিলের সুপারিশ করা হইবে।

মোঃ মাজহারুল ইসলাম
নির্বাহী প্রকৌশলী
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা
ও সদস্য-সচিব,
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।

সাইমুল হক
উপ-বিভাগীয় প্রকৌশলী,
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা
ও সদস্য,
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।

মোঃ আঃ লতিফ
তত্ত্বাবধায়ক প্রকৌশলী
আর.পি.ই. এন্ড এম সার্কেল, ঢাকা ওয়াসা
ও আহ্বায়ক
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।

MIST(ME) REF No: 23.12.0902.006.021.008.31.08.2026/Pump94; DATE: 31-08-2026; MIST(ME) হতে
হতে প্রাপ্ত টেষ্ট রিপোর্টের ভিত্তিতে উপরে উল্লেখিত তালিকার পাম্প মোটর সমূহ যৌথ পরিদর্শন কমিটি কর্তৃক চূড়ান্তভাবে গ্রহণের সুপারিশ করা হল।

মোঃ মাজহারুল ইসলাম
নির্বাহী প্রকৌশলী
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা
ও সদস্য-সচিব,
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।

সাইমুল হক
উপ-বিভাগীয় প্রকৌশলী,
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা
ও সদস্য,
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।

মোঃ আঃ লতিফ
তত্ত্বাবধায়ক প্রকৌশলী
আর.পি.ই. এন্ড এম সার্কেল, ঢাকা ওয়াসা
ও আহ্বায়ক
কারিগরি পরীক্ষণ ও গ্রহন কমিটি।
