



ঢাকা পানি সরবরাহ ও পয়ঃ নিষ্কাশন কর্তৃপক্ষ

নির্বাহী প্রকৌশলীর কার্যালয়
সংগ্রহ বিভাগ-২, ওয়াসা ভবন (৬ষ্ঠ তলা),
৯৮, কাজী নজরুল ইসলাম এভিনিউ, কাওরান বাজার, ঢাকা-১২১৫।

মালামাল পরিদর্শন ও টেষ্ট রিপোর্ট


চুক্তি নং-	৪৬.১১৩.৪২৮.০০.০০.০৯২/২০২৫-২৬/সিএ-২৬;	তারিখঃ ১২/০৪/২৬ ইং।
সরবরাহ আদেশ নং-	৪৬.১১৩.৪২৮.০০.০০.০৯২.২০২৬-৮৫০	তারিখঃ ২৩/০৪/২৬ ইং।
কাজের নাম	Procurement of DN 200mm SCADA Compatible Bulk Water Meter for Dhaka WASA (Lot-2).	
সরবরাহকারীর নাম	এ এম জেড ইনকর্পোরেট, ৫৪, আর. কে মিশন রোড, সূত্রাপুর, ঢাকা-১২০৩, বাংলাদেশ।	
ব্যবহারকারী বিভাগের নাম	মিটার বিভাগ, ঢাকা ওয়াসা।	
সংগ্রহকারী বিভাগের নাম	সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা।	
সরবরাহের স্থান	ভান্ডার বিভাগ, ঢাকা ওয়াসা।	
সরবরাহের তারিখ	২৪/০৯/২০২৬ ইং।	যৌথ পরিদর্শনের তারিখঃ ২৯/০৯/২০২৬ ইং।

ক্র. নং	মালামালের বিবরণ	চুক্তি অনুযায়ী মালামালের পরিমাণ	দেয় মালামালের পরিমাণ	অবশিষ্ট মালামালের পরিমাণ	Country of origin
১।	DN 200mm SCADA Compatible Bulk Water Meter	৩০০টি	৩০০টি	নাই	Spain

যৌথ পরিদর্শন কমিটির বাস্তব (ফিজিক্যাল) পরিদর্শন রিপোর্ট ও স্বাক্ষরঃ

যৌথ পরিদর্শন কমিটি কর্তৃক সমুদয় মালামাল পরিদর্শন করা হইল এবং তা বাহ্যিকভাবে সঠিক পাওয়া গেল। বাহ্যিকভাবে সঠিক পাওয়ায় টেষ্টের জন্য নমুনা সংগ্রহ করা হইল। মিটার বিভাগ, ঢাকা ওয়াসা হইতে প্রাপ্ত টেষ্ট রিপোর্টের ভিত্তিতে সমুদয় মালামাল চূড়ান্তভাবে গ্রহণ/ বাতিলের সুপারিশ করা হইবে।


মোঃ মাজহারুল ইসলাম
নির্বাহী প্রকৌশলী
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা


কাওহার
সহকারী প্রকৌশলী
পিএন্ডডি (যান্ত্রিক ও তড়িৎ) বিভাগ, ঢাকা ওয়াসা


মোঃ আর. লতিফ
তত্ত্বাবধায়ক প্রকৌশলী
আর.পি.ই. এন্ড এম সার্কেল, ঢাকা ওয়াসা

সদস্য-সচিব, কারিগরি পরীক্ষন ও গ্রহন কমিটি।


সদস্য, কারিগরি পরীক্ষন ও গ্রহন কমিটি।


আহ্বায়ক, কারিগরি পরীক্ষন ও গ্রহন কমিটি।

মিটার বিভাগ, ঢাকা ওয়াসা হতে প্রাপ্ত টেষ্ট রিপোর্টের উপর যৌথ পরিদর্শন কমিটির মতামত ও স্বাক্ষরঃ

স্মারক নং-৪৬.১১৩.৪৩৮.০০.০০.২০২৬-৩৯৪; তারিখঃ ১৫/১০/২০২৬খ্রিঃ মোতাবেক মিটার বিভাগ হতে প্রাপ্ত টেষ্ট রিপোর্ট সন্তোষজনক। টেষ্ট রিপোর্ট সন্তোষজনক পাওয়ায় সরবরাহকৃত সমুদয় মালামাল যৌথ পরিদর্শন কমিটি কর্তৃক চূড়ান্তভাবে গ্রহণের সুপারিশ করা হল।


মোঃ মাজহারুল ইসলাম
নির্বাহী প্রকৌশলী
সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা


কাওহার
সহকারী প্রকৌশলী
পিএন্ডডি (যান্ত্রিক ও তড়িৎ) বিভাগ, ঢাকা ওয়াসা


মোঃ আর. লতিফ
তত্ত্বাবধায়ক প্রকৌশলী
আর.পি.ই. এন্ড এম সার্কেল, ঢাকা ওয়াসা

সদস্য-সচিব, কারিগরি পরীক্ষন ও গ্রহন কমিটি।

সদস্য, কারিগরি পরীক্ষন ও গ্রহন কমিটি।

আহ্বায়ক, কারিগরি পরীক্ষন ও গ্রহন কমিটি।

ঢাকা পানি সরবরাহ ও পল্লী নিষ্কাশন কর্তৃপক্ষ



নির্বাহী প্রকৌশলীর কার্যালয়

মিটার বিভাগ, ঢাকা ওয়াসা।

৪/৪, সেগুন বাগিচা, ঢাকা-১০০০।

e-mail: meterdwasa@gmail.com



স্মারক নং-৪৬.১১৩.৪৩৮.০০.০০.২০২৬-৩৯৪

তারিখ : ৩০ আশ্বিন ১৪৩৩

১৫ অক্টোবর ২০২৬

নির্বাহী প্রকৌশলী

সংগ্রহ বিভাগ-২

ঢাকা ওয়াসা।

বিষয় : ০২ (দুই) টি পানির মিটারের পারফরমেন্স টেস্ট রিপোর্ট প্রদান প্রসঙ্গে।

সূত্র : স্মারক নং : ৪৬.১১৩.৪২৮.০০.০০.০৯২.২০২৬-২৫১, তারিখ : ২৯ সেপ্টেম্বর ২০২৬ খ্রিষ্টাব্দ।

উপরোক্ত বিষয় ও সূত্রের প্রেক্ষিতে জানানো যাচ্ছে যে, সংগ্রহ বিভাগ-২ হতে Procurement of DN 200 mm (DN-200) SCADA Compatible Bulk Water Meter for Dhaka WASA (Lot-2) শীর্ষক সংগ্রহ কাজের আওতায় সরবরাহকৃত পানির মিটার হতে ০২ (দুই) টি পানির মিটারের পারফরমেন্স টেস্ট করে রিপোর্ট প্রদানের অনুরোধ জানান। সেই প্রেক্ষিতে সংগ্রহ বিভাগ-২ এর চাহিদা মোতাবেক ২০০ মিঃ মিঃ ০২ (দুই) টি পানির মিটার টেস্ট কার্যক্রম শেষ করা হয়েছে।

এমতাবস্থায়, সরবরাহকৃত ০২ (দুই) টি পানির মিটারের পারফরমেন্স টেস্ট রিপোর্ট পরবর্তী কার্যক্রমের জন্য এতদসঙ্গে প্রেরণ করা হলো।

AE
25.10.26

মোঃ মাহবুব হাসান
নির্বাহী প্রকৌশলী
মিটার বিভাগ
ঢাকা ওয়াসা।
15/10/26

সংযুক্তি :

১। মিটার টেস্ট রিপোর্ট ১ সেট, (০২ (দুই) টি মিটার)।

সদয় অবগতির জন্য অনুলিপি প্রেরণ করা হলো :

- ১। উপ-ব্যবস্থাপনা পরিচালক (ও.এড.এম), ঢাকা ওয়াসা।
- ২। প্রধান প্রকৌশলী, ঢাকা ওয়াসা।
- ৩। প্রধান রাজস্ব কর্মকর্তা, ঢাকা ওয়াসা।
- ৪। তত্ত্বাবধায়ক প্রকৌশলী, (এস.এম.ডব্লিউ.সি) সার্কেল, ঢাকা ওয়াসা।
- ৫। উপ-সহকারী প্রকৌশলী, মোঃ রবিন হাসান, সংগ্রহ বিভাগ-২, ঢাকা ওয়াসা।
- ৬। অফিস কপি।

Office of The Executive Engineer
Meter Division , Dhaka WASA
4/4, Segunbagicha, Dhaka-1000

Meter Test Results

Name of the Test	Performance Test (Discharge)
Name of the Supplier	Pepco Bangladesh

Performance of flow measurement of 200 mm dia water meter (Meter No : 26/020092)				Remarks
No of Observation	Discharge test by master meter (Liter/minute)	Discharge test by tested meter (Liter/minute)	Error (%)	
	A	B	$C=(B-A)/A \times 100$	
1	1890	1885	-0.26%	Satisfactory
2	1940	1920	-1.03%	Satisfactory
3	2080	2030	-2.40%	Satisfactory

Performance of flow measurement of 200 mm dia water meter (Meter No : 26/019810)				Remarks
No of Observation	Discharge test by master meter (Liter/minute)	Discharge test by tested meter (Liter/minute)	Error (%)	
	A	B	$C=(B-A)/A \times 100$	
1	1980	1960	-1.01%	Satisfactory
2	2060	2045	-0.73%	Satisfactory
3	2130	2110	-0.94%	Satisfactory

৭/১২/১৬
২৫/১০/১৬
মোঃ জাহাঙ্গীর আলম
মেকানিক
মিটার ওয়ার্কশপ মিটার বিভাগ

২৫/১০/১৬
মোঃ আব্দুল মান্নান
কোরম্যান
মিটার ওয়ার্কশপ মিটার বিভাগ
ঢাকা ওয়াশা

১৫/১০/১৬
মোঃ রাহাত হোসেন
উপ-সহকারী প্রকৌশলী
মিটার বিভাগ
ঢাকা ওয়াশা

১৫/১০/১৬
মোঃ মাহবুব হাসান
নির্বাহী প্রকৌশলী
মিটার বিভাগ
ঢাকা ওয়াশা



Industry & Facilities Division
Third Party Inspection Report

Page 1 of 13

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001		Revision No. 01
☐ Initial ☐ Interim ☒ Final ☐ Resident ☐ Remote		
Inspection requested by: HIDROCONTA, S.A.U.		
Inspection performed as Recognised Authority:		☐ Yes ☒ No
BV Job Nr: 32455852		

Project: DWASA/Proc2/26 DHAKA WASA Contract Number.: 46.113.428.00.00.092/25-26/CA-26, DWASA.	IPO Ref (If applicable): N/A
Applicant name: AMZ Incorporate	P/o nr: P26001407
BV Client: HIDROCONTA, S.A.U.	END USER: DHAKA WASA
Manufacturer/Vendor: HIDROCONTA, S.A.U.	Previous Inspection (If applicable): N/A
Inspection Location (Address): Carril de la Cierva, 72, 30151 Murcia, Spain	Next Inspection (If applicable): N/A
Inspection Location (GPS Coordinates): 37.94881937849981, -1.1326785000000001	Total No. of Inspection Days: 1
Inspection performed on: July 15, 2026	

MATERIAL / SUBJECT OF INSPECTION	ITEM / TAG Nr	QTY As per P/O	QTY Offered for inspection
☒ Refer to attachment section J instead			
WATER METER PREDATOR (DN200)	-	300	300
SPARE PARTS WATER METER PREDATOR	-	15	15

A – INSPECTION RESULT		
☒ Satisfactory (Without comments)	☐ Satisfactory with comments (Any of trailing Punch or Non Conformity items is still open)	☐ Not Satisfactory (NCR raised during the inspection)
Inspection Summary: (for details refer to section E) Verification of material related to Contract Number.: 46.113.428.00.00.092/25-26/CA-26, DWASA. L/C NUMBER 350226010445 - DATE: 260614 BIN:003511002-0307, TIN:339771711174, IRC NO.260326112086520, H.S.CODE NO.: 9028.20.00, 9028.90.90 (FOR BANGLADESH) AND ISSUING BANK BIN NO. 000001507-0202.		
Open Non Conformities:	☐ Yes, details in section G	☒ No
Open Punch List Items:	☐ Yes, details in section H	☒ No
Release Note Issued:	☐ Yes, number(s):	☒ No
BV Traceability Stamping:	☐ Yes, 	☒ No

BV Inspector: <i>María del Carmen Nicolás Ibáñez</i> 	BV Coordinator: <i>Estefanía Álvarez</i>
BV Office: Murcia, Spain	Inspection Report Date: July 17, 2026
Distribution: ☒ CLIENT ☒ BV ☒ MANUFACTURER ☐ OTHER:	Attachments Report: ☒ Yes, details in section J ☐ No

GM-SI-101 INSP002-En Rev. 3.1

Copyright Bureau Veritas 06/2021

This template is intended exclusively when BV is acting as 3° party inspection body. The use of present template is forbidden in the frame of 2° party services where Client specification and templates must be used.

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001	Revision No. 01
---	-----------------

B - REFERENCE DOCUMENTATION:

☒ Refer to attachment section J instead

Title	Reference n°	Rev.	Approval status	Approved by	Date
Invoice	E26/0095	-	-	-	16/07/2026
Packing List	P26/0144	-	-	-	16/07/2026
Credit Letter	350226010445	-	Approved	CAIXABANK	14/06/2026

C - ATTENDEES

Name	Position	Representing
Antonio Baños	Operations & Purchasing Director	Hidroconta S.A.U.
María del Carmen Nicolás Ibáñez	Inspector	Bureau Veritas

D - MEASURING & TESTING EQUIPMENT USED

☐ Refer to attachment section J instead

Equipment Type	Equipment Identity n°	Last Calibration Date	Expiry Date
Test Bench	BC G2	-	-
Pressure Test Bench	1	-	-
Flexometer	25124	27/06/2025	27/06/2030

E - INSPECTION DETAILS

E - General

The inspection was carried out at the Hidroconta facilities in Murcia on July 15, 2026.

Visual inspection of pallets and water meters was performed. The goods were seen brand new and without damage.

Then, water meters were checked according to Technical Specification of DN 200mm SCADA Compatible Bulk Water Meter. We witnessed accuracy and pressure tests of 6 randomly selected units. We also have reviewed the attached documents (section J).

E1 - Details of Witness (W) & Hold (H) Inspection Points

1. Visual inspection

Visual control was performed on randomly selected 6 pcs water meter PREDATOR DN200. The goods were seen brand new and without damage.

The serial numbers of the water meters inspected are as follows:

Description	Serial No.	Seal No.
PREDATOR DN200 Water meter	26/020002	0614810
	26/020003	0614780
	26/020004	0614863
	26/020007	0614816
	26/020008	0614822



INSPECTION REPORT No. 30-X42-1-32455852-1001-0001

Revision No. 01

26/020011

0602902

2. Technical specifications of Water Meters were checked according to Technical Specification of DN 200mm SCADA Compatible Bulk Water Meter

Details are given below:

SI No.	Specifications	Remark / Result
1.	General The water meters shall be used to record potable water flow within transmission and distribution systems as well as source supply installations. The supplier shall furnish all goods and supplies and conduct performance testing as specified herein.	Verified.
2.	Standards All goods and workmanship throughout should, where applicable, comply with the latest provisions of ISO standards or codes of practices as specified herein. Meter must confirm to the latest version of ISO 4064/01 ML R49/MID or equivalent AWWA standard. Meters must conform to ISO 9001: 2000 (Latest version) certificates with latest Audit report and an environmental management certificate, preferably ISO-14001 of the proposed manufacturers, as well as the EEC Directive 75/33 or MID (where superseded 2004/22/EC) or equivalent AWWA or OIML certificate of standard compliance of water meter. And have at least 10 (ten) years' experience in manufacturing meters. Meters shall be suitable for use with water having the following characteristics: Fe up to 5mg/l Mn up to 1mg/l Chloride up to 500mg/l Conductivity up to 1,000µS/cm pH 6.5 to 8.5 Alkalinity up to 220mg/l Temperature up to 30°C Free chlorine up to 25ppm	Water meters type PREDATOR complies with the requirements of the Directive 2014/32/EU. The equipment has successfully overcome the test made under the standards OIML R49-1/-2 and UNE-EN ISO 4064-1/-2. The manufacturer is ISO 9001:2015 and 14001:2015 certified. See attachments #3, #4, #5, #6. Water meters meet the requirements of the DIN 50930 standard. See attachment #9.
3.	Marking The following information shall be marked in an indelible manner on the meter register: Year of manufacture. Direction of flow (mechanical meters) The name of the manufacturer. Individual serial number in one place. Nominal flow rate in m ³ /h. Maximum working pressure in bars. Size in mm. Stamp ISO or other certification.	Verified.



INSPECTION REPORT No. 30-X42-1-32455852-1001-0001	Revision No. 01
---	-----------------

		The letters 'DWASA'.		
4.	Sizes	Mechanical Meters: Meter sizes shall be as given in the List of Goods and Related Services.	DN200 (200mm).	
5.	Manuals	For each size of meter the supplier shall furnish 10 (ten) copies of complete meter manual booklets for installation, operation and maintenance.	Verified. 10 copies of instructions manuals are included.	
6.	Warranty	Water meters shall be designed for a lifetime of at least 10 years under normal operating conditions. Tenderer shall provide 1 (one) year warranty on the meter against material defects, workmanship and design defects. In case of loss of meter accuracy or any defect with the installed meter, the Supplier shall replace the defective meter with new one within 15 days of instruction from the Purchaser against the above stated warranty condition.	The water meter model PREDATOR supplied have a warranty against material defects, workmanship and design defects for 28 months after shipping date or 24 months after acceptance those meters by Dhaka Wasa, whichever occurs first. In case of loss of meter accuracy or any defect with the installed water meter, HIDROCONTA, S.A.U. will replace the defective water meter with new one within 15 days. See attachment #10 Manufacturer's Warranty Statement.	
7.	Pulse Outputs	Pulse Outputs Meters shall be able to generate a pulse directly from the register to allow automatic meter reading (AMR), logging or installation of a remote meter head. It shall be possible to generate a pulse at the rate of at least 1 per 100/1000 liters. The tenderer shall indicate clearly in the tender how AMR can be implemented directly using the type of meter proposed. A cable shall be supplied and attached to the meters for pulse transmission and shall not be less than 2 meters in length.	AMR verified by accuracy testing. 1 pulse per 100 liters. See attachment #14.	
		The Meter's register integrity to IP68 shall not be compromised by any such pulse output which shall also operate under submerged conditions.	Verified by dimensional control. Wire is 2,4m long.	
			Due to dimensions of water meters DN200, it was not possible to perform the test at the Hidroconta facilities. See attachment #7 Manufacturer's IP68 Protection Statement.	
8.	Tools	The supplier shall supply 10 complete sets of standard tools with boxes for repair and maintenance of the meters.	No specific tools are need for repair or maintenance of the water meters. See attachment #11 Manufacturer's No Special Tools Required Statement.	
9.	Transport and	The finished materials should be packed for	Verified.	

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001			Revision No. 01
	Packing	worthy handling following international standard suitable for tropical climate. Also should be protected from damage during handling and delivery. All loose items should be carefully packaged to protect during storage. Each package should be carefully marked as to contents, quantity and date of packaging in an indelible manner.	
10.	Manufacturers authorization	Documentation to confirm that all delivered goods and equipment supplied have been tested at the manufacturer's factory to the required working conditions and/or function and that the quality of manufacture meets all mentioned international standards.	CE declaration of conformity. See attachment #3.
11.	Testing and calibration	All water meters shall be delivered fully tested, calibrated and sealed according to ISO standard 4064 or any equivalent other international accepted standard.	CE declaration of conformity. See attachment #3.
12.	Materials & Construction	Water meters shall be of horizontal helix wet Woltmann type with completely waterproof encased gear train, magnetic transmission and registration, shielded against tampering or any external magnetic field. The inlet and outlet shall have a common axis.	Verified. See attachment #9.
		The water meter body shall be made of grey or ductile cast iron. Flanges shall be drilled according to DIN 2501 PN10 or PN 16. For the measurement unit an approved synthetic material shall be used. Meters shall have a means of adjustment to allow calibration. This may be operated externally or internally on the meter impeller. The meter impeller shall be easily removed from the meter housing to allow such adjustment.	PN16. The material used in the bodies complies with the requirements established in standard DIN 50930. See attachment #9 Test Report Statement for Water Meters PREDATOR.
		All parts in contact with the water shall have smooth surfaces, protected where necessary to prevent encrustation. The quoted flow meters shall be suitable for horizontal installation. The tender must include all materials required for proper installation.	See attachment #12 Manufacturer's Durability Statement.
13.	Performance requirements	Meters shall conform to class B accuracy. a. Nominal Diameter- 200 mm b. Minimum flow rate Q1- 4.0 m3/hr c. Transitional flow rate Q2- 6.4 m3/hr d. Permanent flow rate Q3- 400 m3/hr e. Overload flow rate Q4- 500 m3/hr Measurement errors between Q4 and Q2 shall not exceed +/- 2%. Measurement errors between Q2 and Q1 shall not exceed +/- 5%.	Verified. Accuracy Test witnessed. Q1- 4.0 m3/h --- Max. error: - 3.95% Q2- 6.4 m3/h --- Max. error: - 1.97% Q3- 630 m3/h --- Max. error: - 0.95% See attachment #14.

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001			Revision No. 01
14.	Accessibility	Meters shall have a modular design. The measuring insert shall be removable and rapidly exchangeable without removing the body from the pipe work. Meters shall have readily accessible change gears, adjustable vanes or other approved means to adjust meter registration. Such adjustment feature shall be an integral part of the removable, rotor/register assembly and not of the main or bottom case of the meter.	Verified.
15.	Register	The register shall be dry and be hermetically sealed and water tight to IP68. The registers shall be straight reading totalizer with roller type mechanism and should be designed such that after recording full capacity it will automatically revert to zero. The unit symbol m ³ should be shown on the dial. The dial should have a hinged hood for protection.	The water meter meets the IP68 rating. See attachment #7. The unit symbol is m ³ . The dial should have a hinged hood for protection.
		The register shall be capable of recording the following: Diameter 150-300 (mm): Interval 0.005 (cubic meter): Max. reading 9.999.999 (cubic meter)	Verified. DN200. The smallest graduation is 0.002 m ³ . Max. reading 9.999.999 m ³ .
16.	Remote Register	It shall be possible to install a remote meter register not less than 2 meters from the meter body using a pulse output. Supplied remote registers shall be wall mountable.	Verified. Wire is 2,4m long.
17.	Pressure	The working pressure (maximum admissible pressure) shall not be less than 16 bar and shall conform to the testing in accordance with ISO-4064. The meter shall be tested at 25 bar with no leakage. The supplier shall provide test results to prove that the meters perform to the accuracy specified above.	Verified. Pressure test on 6 units was witnessed. 25 bar for 1 minute with satisfactory results.
18.	Head Loss	The loss of pressure through the meter must conform to ISO-4064 or equivalent.	Pressure loss Class $\Delta P16$ (0.16 bar), according to technical characteristics included in EU Type Examination Certificate.
19.	Sealing	The meters shall be equipped with a tamper-proof device consisting of a water proof synthetic thread/seal wire and lead seal which must be broken in order to remove the register box and calibrating cap nut.	Verified.
20.	Coatings	Materials shall be selected to have adequate mechanical, chemical and electrochemical resistance against abrasion and corrosion. Where necessary metallic parts of the meters shall have corrosion resistant coating applied suitable for a tropical humid environment. Materials shall be selected to have adequate mechanical, chemical and	See attachment #9 Test Report Statement for Water Meters PREDATOR.



INSPECTION REPORT No. 30-X42-1-32455852-1001-0001	Revision No. 01
---	-----------------

		electrochemical resistance against abrasion and corrosion. Materials in contact with the water shall be non-toxic and shall not affect the quality of the water.	
21.	Spares	The supplier shall supply the following spare parts: Meter registers: 5% of total meters.	Pallet #18 contains 15 boxes with spare parts.

E2 – Details of Monitoring and Surveillance Patrols

☐ Tick if conducted during the visit

N/A

E3 – Details of Certificates Review

☒ Tick if conducted during the visit

- ISO 9001:2015 Certificate N° ES-0362/2000 (Validity date: 2027-03-17)
- ISO 14001:2015 Certificate N° ES-2024/0074 (Validity date: 2027-03-17)
- EU Type Examination Certificate N° 0300-ES-182140001 (Validity date: 2029-01-02)
- Warranty Certificate

F – HEALTH, SAFETY & ENVIRONMENT COMMENTS

All participants were briefed about safety and PPE requirements.

G- NON CONFORMITIES

☐ Refer to attachment section J instead

Item	Description	Status	Raised on	Report Nr.	Closed on	Report Nr.	Comments
N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A

H – PUNCH LIST ITEMS

☐ Refer to attachment section J instead

Item	Description	Status	Raised on	Report Nr.	Closed on	Report Nr.	Comments
N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A



INSPECTION REPORT No. 30-X42-1-32455852-1001-0001

Revision No. 01

I - DIGITAL PICTURES



Pallet #1



Pallet #7

GM-SI-101 INSP002-En Rev. 3.1

This template is intended exclusively when BV is acting as 3° party inspection body.




Copyright Bureau Veritas 06/2021

The use of present template is forbidden in the frame of 2° party services where Client specification and templates must be used.

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001


Revision No. 01

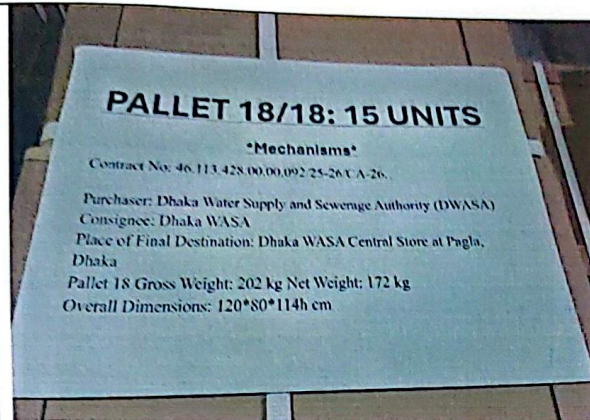


Pallet labelling



Package water meter DN200

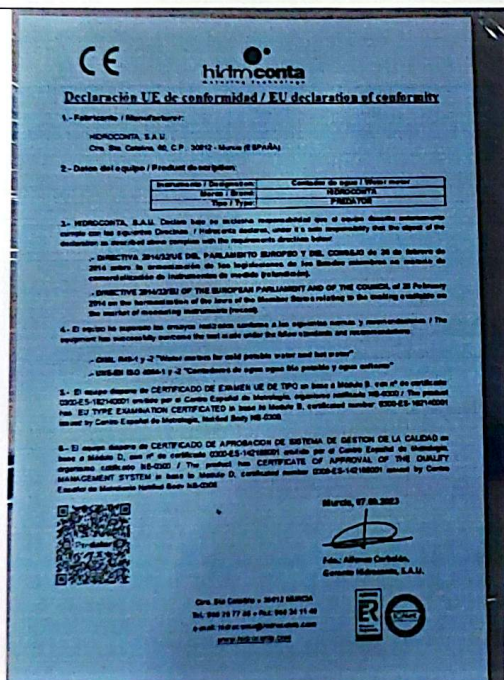

CE declaration of conformity (included inside box)

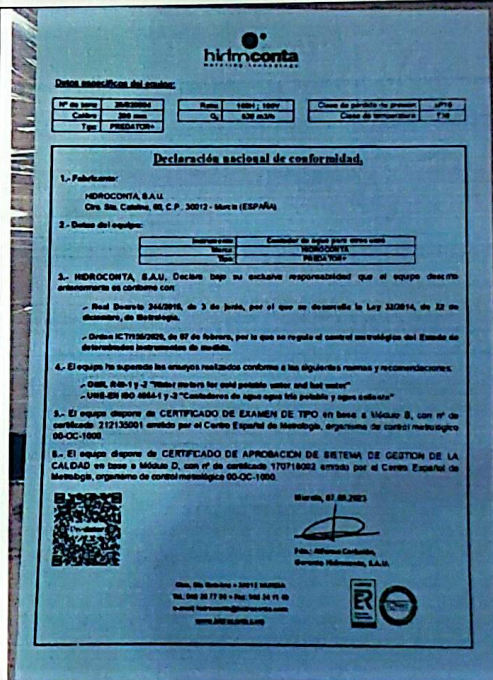


National declaration of conformity (included inside box)

INSPECTION REPORT No. 30-X42-1-32455852-1001-0001


Revision No. 01



Marking – water meter DN200

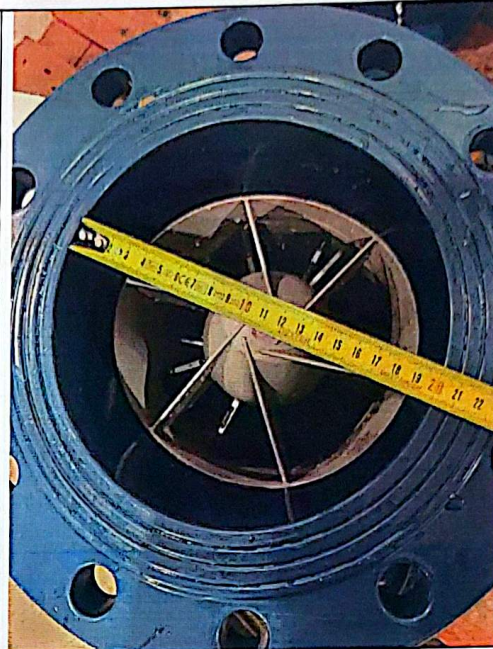

Dimensional check (DN200)

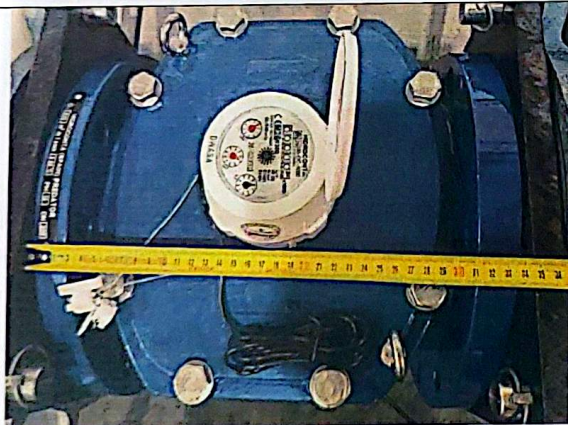

Dimensional check (350mm length)



Water meter with seals

GM-SI-101 INSP002-En Rev. 3.1

This template is intended exclusively when BV is acting as 3° party inspection body.



Copyright Bureau Veritas 06/2021

The use of present template is forbidden in the frame of 2° party services where Client specification and templates must be used.
